

 NEW YORK STATE
 Department of Environmental Conservation
 Image: Conservation

 WESTERN BAYS CONSTRUCTORS PICONE
 NORTHEAST REMSCO

March 2024

CONSTRUCTION LOOK AHEAD

Note: The Project work locations and description of activities explained below are dynamic and subject to change. Visit our Facebook page @BayParkConveyance for weekly and more frequent updates regarding project activities, locations, and lane closures. Call the 24/7 Project Hotline at (516) 252-6121 with concerns and questions. Text "roadwork" to "888777" to receive updates on County-wide daily road and lane closures.



PROGRESS SUMMARY

- Work is ongoing at the South Shore Water Reclamation Facility (WRF) and the Cedar Creek Water Pollution Control Plant (WPCP).
- Sliplining is complete and final roadway restoration continues across Sunrise Highway.
- Microtunneling is complete. Backfilling and restoration activities are ongoing at various shaft sites across the microtunneling alignment.
- Hydrostatic testing to ensure the new pipeline meets Project plans will continue in March at select pit and shaft sites.
- Landscape restoration activities are anticipated to begin in spring 2024. Restoration plans are available on our website.

SOUTH SHORE WRF UPDATES

- In March, crews will continue final roof construction and install architectural panels on the exterior of the effluent diversion pump station building.
- Inside the building, crews continue to paint and install electrical and plumping in preparation for the pumps.

CEDAR CREEK WPCP UPDATES

- Crews continue work on the receiving tank structure and completed installation of the pipeline connecting the tank to Cedar Creek Shaft 1.
- Work is progressing to support the wet tap to connect the new conveyance infrastructure with the existing outfall.



Exterior of the new Effluent Diversion Pump Station at SSWRF (January 2024)



MICROTUNNELING •



March 2024

In the immediate areas surrounding Bay Park and Cedar Creek shaft sites, residents will notice an increase in construction vehicles and crews. WBC will continue to monitor and control any potential noise, dust, vibrations, and settlement from construction activities. Unless otherwise specified, work activities are expected to occur Monday through Friday, between 6 a.m. to 5 p.m. Some weekend work is expected in March.

BAY PARK

Microtunneling is complete along the Bay Park alignment. However, residents may notice the following activities:

- Restoration activities will continue at Bay Park Shafts 2, 3 and 4.
- Crews are working below the ground in the pipeline, inspecting the pipe and testing joint connections. This work is performed in advance of the more rigorous hydrostatic testing.
- Hydrostatic testing of the new pipeline will begin at Bay Park Shafts 1 and 5.



Receiving Tank Structure Progress (January 2024)



Cedar Creek Shaft 2 Manhole Installation (February 2024)

CEDAR CREEK

Microtunneling is complete along the Cedar Creek alignment. However, residents may notice the following activities:

- Crews are working below the ground in the pipeline, inspecting the pipe and testing joint connections. This work is performed in advance of the more rigorous hydrostatic testing.
- Hydrostatic testing of the new pipeline will soon begin at Cedar Creek Shafts 1 and 3.
- Crews completed installation of a riser pipe at Cedar Creek Shaft 6 in preparation for hydrostatic testing.



Regrading at Bay Park Shaft 5 (January 2024)






March 2024

FINAL ROADWAY RESTORATION

For the duration of the Project, we ask for your cooperation adhering to traffic safety along work zone areas. Western Bays Constructors (WBC) is coordinating with New York State Department of Transportation (NYSDOT) to communicate lane closures on their Variable Message Signs (VMS). WBC is also communicating with Nassau County Traffic Management about weekly lane closures. The locations, dates, and hours of operation are shared with the public through the Project's Facebook page. Work at select Pit locations will take place overnight Monday through Friday, from 9 p.m. to 6 a.m. During these hours, two eastbound lanes will be closed, and one eastbound lane will remain open. In addition, temporary single lane closures on Sunrise Highway may occur during the day to support construction at Pit W and other locations. WBC will continue to monitor and control any potential noise. vibrations, and settlement from construction activities.

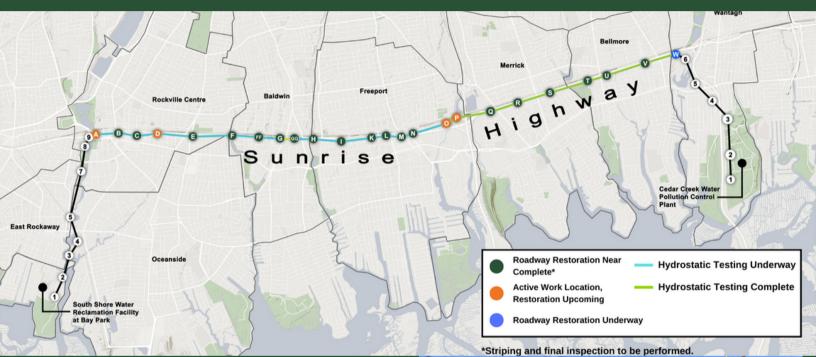

Roadway Restoration Progress

- Roadway restoration is near complete at all roadway pit locations along Sunrise Highway.
- Restoration activities will continue at Pit W throughout the month.
- Additional activities including hydrostatic testing, line striping, and manhole and vent pipe construction continue.
- Pits A, D, O and P are off the roadway and landscape and site restoration plans are underway.



Final Roadway Restoration at Pit GG in Baldwin



Community Information Center 265 Sunrise Highway Rockville Centre, NY 11570 *By Appointment Only



(516) 252-6121

bayparkconveyance@gmail.com

24/7 Project Hotline



Website www.bayparkconveyance.org



Facebook @BayParkConveyance
