

# CONSTRUCTION LOOK AHEAD

Note: The Project work locations and description of activities explained below are dynamic and subject to change. Visit our Facebook page @BayParkConveyance for weekly and more frequent updates regarding project activities, locations, and lane closures. Call the 24/7 Project Hotline at (516) 252-6121 with concerns and questions. Text "roadwork" to "888777" to receive updates on County-wide daily road and lane closures.



## PROGRESS SUMMARY

- Work is ongoing at the South Shore Water Reclamation Facility (WRF) and the Cedar Creek Water Pollution Control Plant (WPCP).
- Sliplining is complete and final roadway restoration is underway across Sunrise Highway.
- Hydrostatic testing to ensure the new pipeline below Sunrise Highway meets Project plans and specifications is ongoing between Pit A to Pit O.
- Backfilling and restoration activities are ongoing at various shaft sites across the microtunneling alignment.
- Landscape restoration activities are anticipated to begin in spring 2024.

## SOUTH SHORE WRF UPDATES

- In January, crews will continue final roof construction at the effluent diversion pump station. Once the pump station building is fully enclosed, crews will work on electrical and pump installation.
- Crews are painting the interior building.

Interior of the new Effluent Diversion Pump Station at SSWRF (November 2023)



## CEDAR CREEK WPCP UPDATES

- Crews continue work on the receiving tank structure. Crews are installing a pipeline connecting the receiving tank to Cedar Creek Shaft 1.
- Excavation is complete and work is progressing in the wet tap area.



# MICROTUNNELING

*In the immediate areas surrounding Bay Park and Cedar Creek shaft sites, residents will notice an increase in construction vehicles and crews. WBC will continue to monitor and control any potential noise, dust, vibrations, and settlement from construction activities. Unless otherwise specified, work activities are expected to occur Monday through Friday, between 6 a.m. to 5 p.m. Some weekend work is expected in January.*

## BAY PARK

**As microtunneling work nears completion along the Bay Park alignment, residents may notice the following activities:**

- Restoration activities will continue at Bay Park Shafts 2 and 3.
- Backfilling and restoration activities will begin at Bay Park Shaft 4.
- Grouting and other activities will continue at select shaft sites.
- Hydrostatic testing of the new pipeline will begin at Bay Park Shafts 1 and 5.



Regrading Activities at BP3 (November 2023)

## CEDAR CREEK

**As microtunneling work nears completion along the Cedar Creek alignment, residents may notice the following activities:**

- Restoration activities will continue at Cedar Creek Shaft 2.
- Hydrostatic testing of the new pipeline will begin at Cedar Creek Shafts 3 and 6.
- Installation of a rise pipe will continue at Cedar Creek Shaft 6 in advance of the hydrostatic testing.



Bay Park Shaft 7 Site (November 2023)




Inspecting the Microtunneling Pipeline (November 2023)



# FINAL ROADWAY RESTORATION


For the duration of the Project, we ask for your cooperation adhering to traffic safety along work zone areas. Western Bays Constructors (WBC) is coordinating with New York State Department of Transportation (NYSDOT) to communicate lane closures on their Variable Message Signs (VMS). WBC is also communicating with Nassau County Traffic Management about weekly lane closures. The locations, dates, and hours of operation are shared with the public through in-person outreach, e-mails, and the Project's website and Facebook page. Work at select Pit locations will take place overnight Monday through Friday, from 9 p.m. to 6 a.m. During these hours, two eastbound lanes will be closed, and one eastbound lane will remain open. In addition, intermittent daytime work may take place and temporary single lane closures on Sunrise Highway may occur during the day to support construction at Pit W and ensure the safety of the traveling public. WBC will continue to monitor and control any potential noise, vibrations, and settlement from construction activities.

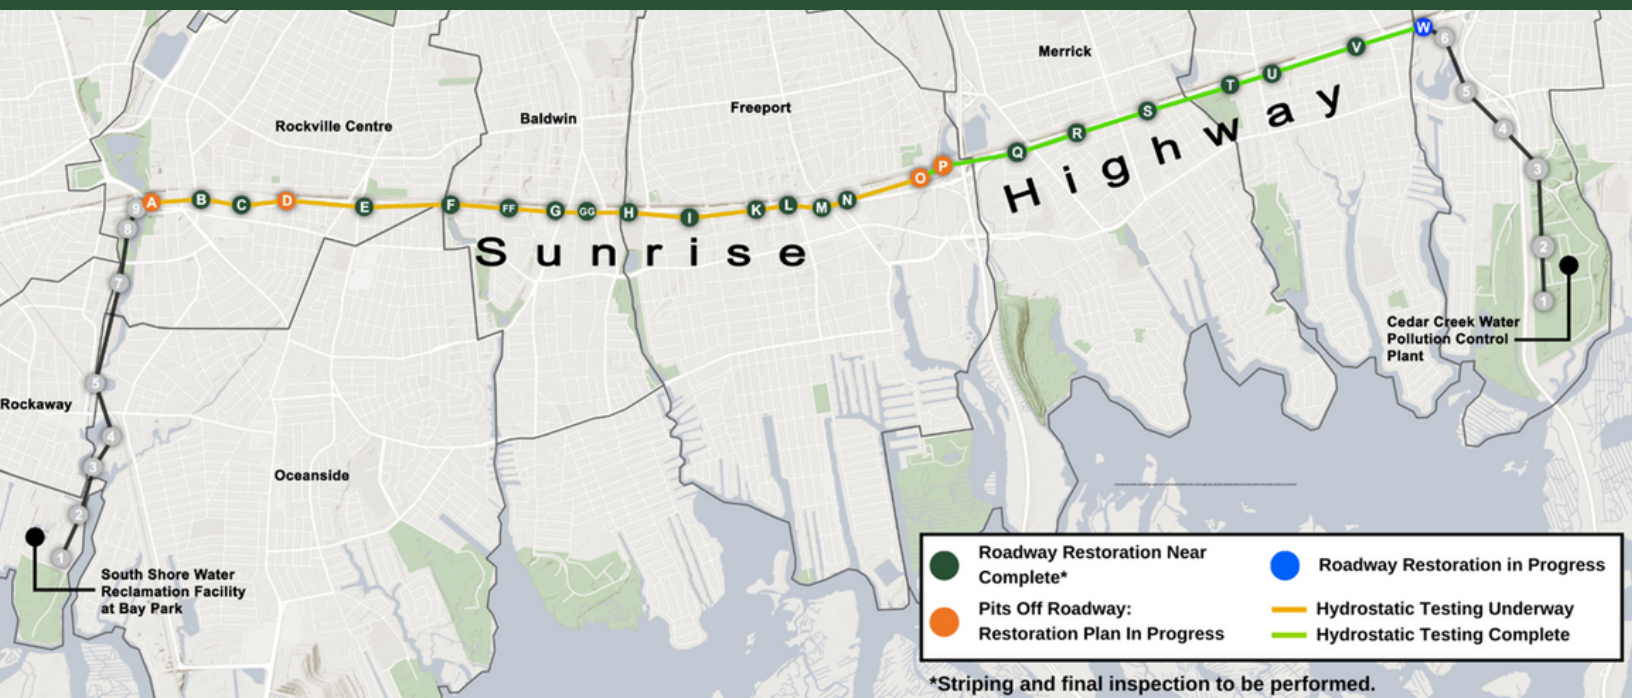


## Roadway Restoration Progress

- Roadway restoration is near complete at all roadway pit locations along Sunrise Highway.
- Restoration activities will continue at Pit W throughout the month.
- Additional activities including hydrostatic testing, line striping, and manhole and vent pipe construction continue.
- Pits A, D, O and P are off the roadway and landscape and site restoration plans are underway.




 **24/7 Project Hotline**  
(516) 252-6121

 **Email**  
[bayparkconveyance@gmail.com](mailto:bayparkconveyance@gmail.com)

 **Website**  
[www.bayparkconveyance.org](http://www.bayparkconveyance.org)

 **Facebook**  
[@BayParkConveyance](https://www.facebook.com/BayParkConveyance)

 **Community Information Center**  
265 Sunrise Highway  
Rockville Centre, NY 11570  
\*By Appointment Only
